



Peirce Island WWTF Upgrade Construction  
Public Information Meeting  
December 19, 2018

## Topics of Discussion

- Introductions
- Work Completed Since Last Meeting
- Work to be Completed in Coming Month
- Work Anticipated in Next 6 Months
- Project Construction Costs
- Events & Recreation
- Public Input/Comments/Concerns
- Next Meeting



# Introductions


- City Staff:
  - Terry Desmarais, City Engineer, 603-766-1421  
tldesmarais@cityofportsmouth.com
- Website:  
<https://www.cityofportsmouth.com/publicworks/wastewater/peirce-island-wastewater-facility/peirce-island-wastewater-facility-upgrade-project>
  - News and Updates
  - Recreational Info
  - Project Info
  - Report Form
  - Etc.

December 19, 2018



Peirce Island WWTF Upgrade Construction

3

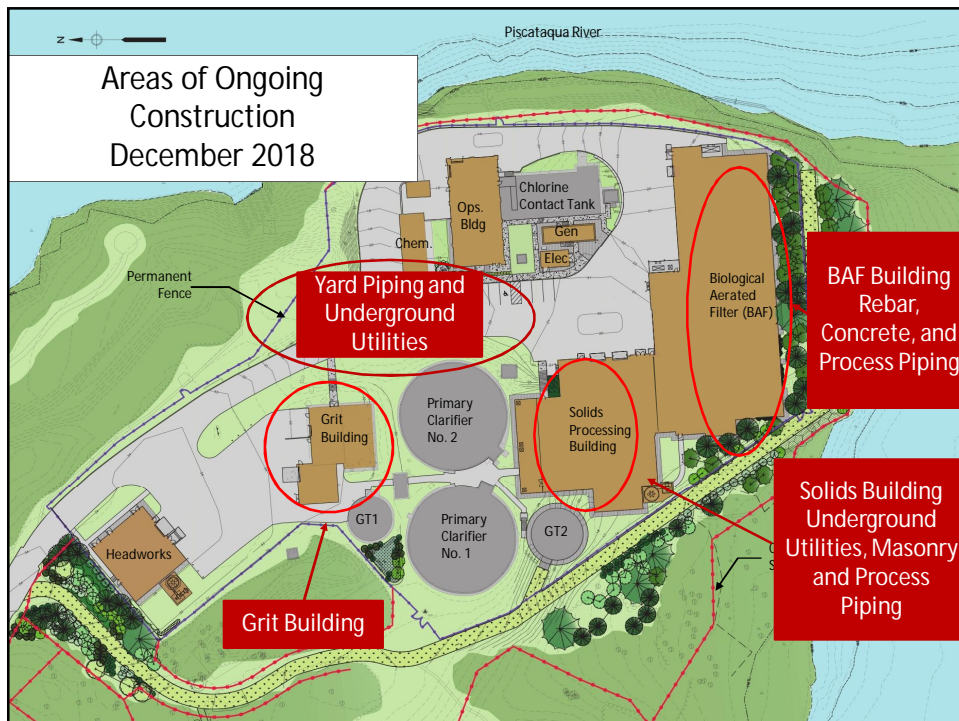

# Site Overview November 2016



December 19, 2018



Peirce Island WWTF Upgrade Construction

5

# Work Completed Since Last Meeting

Solids Building  
Rebar, Concrete,  
and Process  
Piping

Grit Building

BAF Building  
Rebar,  
Concrete,  
Masonry and  
Process Piping

Yard Piping &  
Underground  
Utilities


December 19, 2018



Peirce Island WWTF Upgrade Construction

6

## Work Completed Since Last Meeting

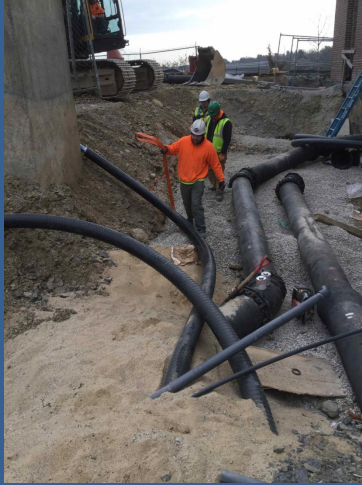

Yard Piping & Utilities

December 19, 2018



Peirce Island WWTF Upgrade Construction

7

## Work Completed Since Last Meeting



Grit Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

8

## Work Completed Since Last Meeting



Grit Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

9

## Work Completed Since Last Meeting



BAF Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

10

# Work Completed Since Last Meeting



BAF Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

11

# Work Completed Since Last Meeting



BAF Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

12

# Work Completed Since Last Meeting



Solids Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

13

# Work Completed Since Last Meeting



Solids Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

14

## Work Completed Since Last Meeting



Solids Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

15

## Work to be Completed in Coming Month

- Continue minor finish work at the Headworks Building
- Continue architectural, structural, mechanical process, HVAC, plumbing, and electrical construction in the Grit Building
- Continue work on process equipment installation in Aerated Grit Chamber No. 2
- Continue installation of reinforcing steel and concrete for the BAF Building slabs and walls
- Continue installation of process piping in Stage 2 of the BAF Building
- Continue installation of process piping in the BAF Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

16



## Work to be Completed in Coming Month, Cont.


- Continue masonry and roofing work on Solids Building
- Continue installation of equipment and process piping in the Solids Building lower level
- Continue underground piping installation between the Grit Building, Solids Building, and BAF Building

December 19, 2018



Peirce Island WWTF Upgrade Construction

17

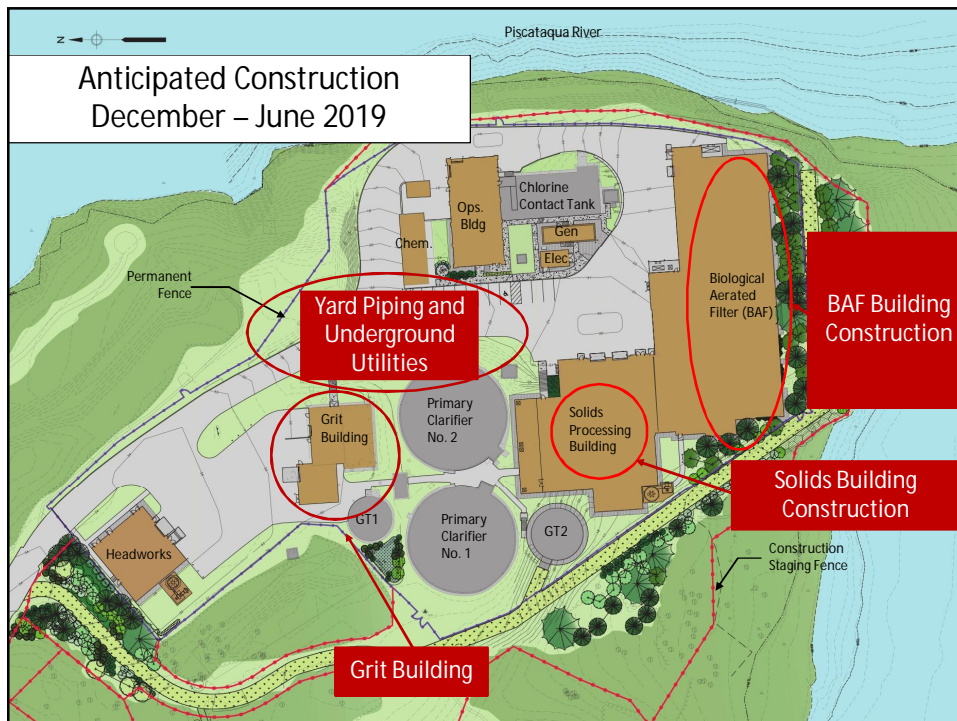

## Project Construction Costs

- Original Contract: \$72.786 million
  - Change Order No. 1: \$0.367 million
  - Change Order No. 2: \$0.547 million
  - Change Order No. 3: \$0.093 million
  - Change Order No. 4: \$0.163 million
  - Change Order No. 5: \$0.250 million
  - Change Order No. 6: \$0.292 million (pending)
- Total Contract: \$74.498 million

December 19, 2018



Peirce Island WWTF Upgrade Construction

19

## Consent Decree Schedule

Milestone	Date	Status
Execute Contract to Construct Upgrades	September 1, 2016	Complete
Submit Two Additional Milestones for EPA Review and Approval	December 1, 2016	Complete
Additional Milestone 1: Transfer of the existing SCADA system to the new Headworks Building	November 21, 2017	Complete
Additional Milestone 2: Startup and testing of the Secondary Influent Pump Station in the new Solids Building	May 9, 2019	On Schedule
BAF Substantial Completion	December 1, 2019	On Schedule
Achieve Compliance with NPDES Permit Limits	April 1, 2020	On Schedule

December 19, 2018



Peirce Island WWTF Upgrade Construction

20

# Events and Recreation

- Upcoming
  - Pro Portsmouth's First Night 2019
  - Strawberry Banke Events

December 19, 2018



Peirce Island WWTF Upgrade Construction

21



Public Input / Comments / Concerns

# Next Meeting

- Public Construction Meeting
  - Next Meeting: January 16, 2019, 11:00 AM

